

2008 Summer Maintenance & Capacity Expansion Programme

Contents

- ◆ Status of scheduled maintenance for April & May
- ◆ Changes to ASEP capability
- ◆ Publication of updates

Maintenance starting in April 2008

Compressor Station Outages	Dates	LDZ	Maintenance Description	Status
Warrington	01/04 -30/09	NW	Routine Maintenance & Control System Replacement	Underway
Kirriemuir	07/04 – 18/05	SC	Routine Maintenance	Delayed until 14/04
Pipeline Work	Dates	LDZ	Maintenance Description	Status
Feeder 14	10/04 – 12/04	SW	Tie in new block valve at Aylesbeare – S. West Reinforcement Project	On Schedule
Feeder 20	28/04 – 29/04	SW	Tie in new block valve at Aylesbeare – S. West Reinforcement Project	Brought forward from June
Feeder 20	30/04 – 31/04	SW	Ottery St Mary – Tie in new feeder 20 to new AGI pipework - S. West Reinforcement Project	Brought forward from June
Feeder 28	14/04 – 20/04	WS	Herbranston AGI – Tie in South Hook LNG	Delayed- new dates tba
On line inspections	Dates	LDZ	Maintenance Description	Status
Feeder 16	28/04 – 04/05	NW	Barrow to Lupton	On Schedule

Pipeline Tie in



Pipeline Tie in (Welding)




Maintenance starting in May 2008

Compressor Station Outages	Dates	LDZ	Maintenance Description	Status
Aylesbury	05/5 – 18/05	SC	Routine Maintenance	On Schedule
Cambridge	12/05 – 25/05	EA	Routine Maintenance	On Schedule
Pipeline Work	Dates	LDZ	Maintenance Description	Status
Feeder 5	01/04 – 04/06	EA	A14 Diversion works (work started in April – actual diversion May)	On Schedule
Feeder 18	06/05 – 08/05	SE	Gravesend – P18 inspection prior to Hot tap connection in July	On Schedule
Feeders 2	12/05 – 23/06	SW	Treadow PRI – Feeder 2 Shutdown for tie-in works	Start date now 5/5
Feeder 7	19/05 – 31/05	SO	Tie in of new feeder 9 from Barton Stacey at Lockerley Compressor	On Schedule
Feeder 7	19/05 – 31/05	SO	Lockerley minimum offtake connection	On Schedule
Feeder 20	01/05 – 02/05	SW	Commissioning of new feeder 20 from Ottery to Aylesbeare - S. West Reinforcement Project	Brought forward from June
Feeder 20	19/05 – 25/06	SW	Aylesbeare – Validate new block valve and perform RVOs	Delayed new dates TBA
Feeders 2 & 23	05/05 – 31/05	SW	Peterstow MJ - Construct & commission common header linking 2 feeders	Completed early

Maintenance starting in May 2008 cont...

On line Inspections	Dates	LDZ	Maintenance Description	Status
Feeder 15	05/05 – 18/05	NW	Lupton to Bretherton	On Schedule
Feeder 15	19/05 – 01/06	NW	Bretherton to Warburton	On schedule

Pipeline Inspection Gauge and P.I.G Trap

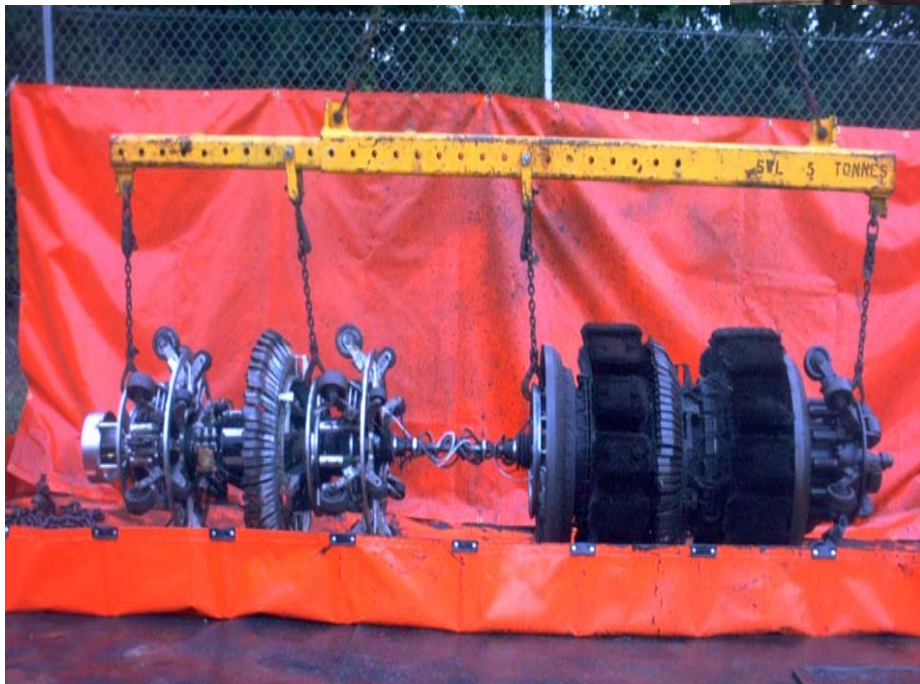

nationalgrid

Changes to capability

- ◆ Currently there are no changes to the capability figures published within the Summer Maintenance plan on the NG Website

Published Maintenance plan

- ◆ The Final Maintenance was plan published on 15th March 200.
- ◆ It has now been updated with the changes detailed today.
- ◆ It can be found on the National Grid Website, as follows: -
 - ◆ www.nationalgrid.com/uk
 - ◆ Energy & Services
 - ◆ Gas
 - ◆ Operational Data
 - ◆ Maintenance Programme / Deliverability
